

REHABILITATION OF CAMERON STREET, EARL STREET, AND VERA CRESCENT

June 21, 2023

Dear Resident,

Schedule Update


H&H Construction's original schedule indicated that the remaining work would take approximately 5 weeks to complete. H&H Construction concentrated on repairing the major deficiencies which has delayed their completion date.

H&H Construction's latest schedule consists of the following:

Asphalt Removal: June 26th
Granular Installation & Grading: June 27th to 30th
Paving - Roadway: July 3rd
Driveway Reinstatements: Week of July 10th
Shouldering: Week of July 10th
Line Painting: Week of July 10th

Deficiencies

H&H Construction will also be continuing to complete deficiencies but if you have a major concern or issue, please contact the project manager listed below.

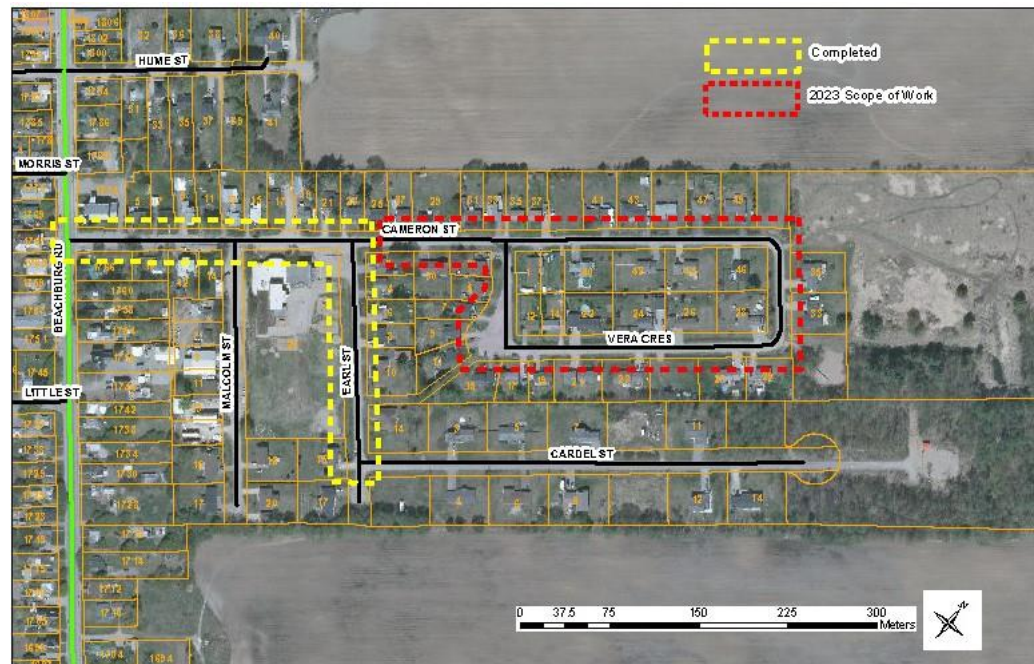

(613) 646-2282

P.O. Box 40
44 Main Street
Cobden, ON
K0J 1K0

www.whitewaterregion.ca



PUBLIC NOTICE

**REHABILITATION OF CAMERON
STREET, EARL STREET, AND VERA
CRESCENT**

Questions and Concern

H&H Construction, Council and Township staff would like to thank for your patience with the construction project. If you have any concerns related to the project, please let us know by contacting the project manager noted below.

Lane Cleroux
Manager of Public Works
Phone: (613) 646-2282 ext. 128
E-mail: lcleroux@whitewaterregion.ca



(613) 646-2282

P.O. Box 40
44 Main Street
Cobden, ON
K0J 1K0



www.whitewaterregion.ca

