

REHABILITATION OF CAMERON STREET, EARL STREET, AND VERA CRESCENT

October 14, 2022

Dear Resident,

Schedule Update

H&H Construction is approximately three to four weeks behind their original schedule. Currently, H&H Construction progress is as follows:

- Watermain: 100% complete
- Storm Sewer: 100% complete
- Road excavation and base installation: 75% Complete
- Culverts: 50% complete
- RCDSB parking lot: 50% complete
- RCDSB Malcolm Street parking area: 100% complete
- Sidewalk: 70% completed
- Curbs: 0% completed
- Paving: 0% completed
- Pathway: 0% completed

Construction Timelines

H&H Construction has requested to defer a portion of Cameron Street and Vera Crescent until spring 2023 due to subgrade concerns. These areas have been significantly disturbed due to construction activities and H&H Construction's experience with these types of soils, is that left for a period of time, the road base will stabilize to allow for the surface works to be completed to a superior standard.

Jp2g and their geotechnical consultant have reviewed H&H Construction's concern and recommend deferring these areas until spring of 2023.

As shown in the map below, Cameron Street from Beachburg Road to Earl Street and Earl Street will be paved and landscaped this fall. Cameron Street from Earl Street to Vera Crescent and Vera Crescent will be completed in spring of 2023. The existing asphalt will remain, and any culvert/ service crossings will be temporary paved for the winter.



(613) 646-2282


P.O. Box 40
44 Main Street
Cobden, ON
K0J 1K0



www.whitewaterregion.ca



REHABILITATION OF CAMERON STREET, EARL STREET, AND VERA CRESCENT

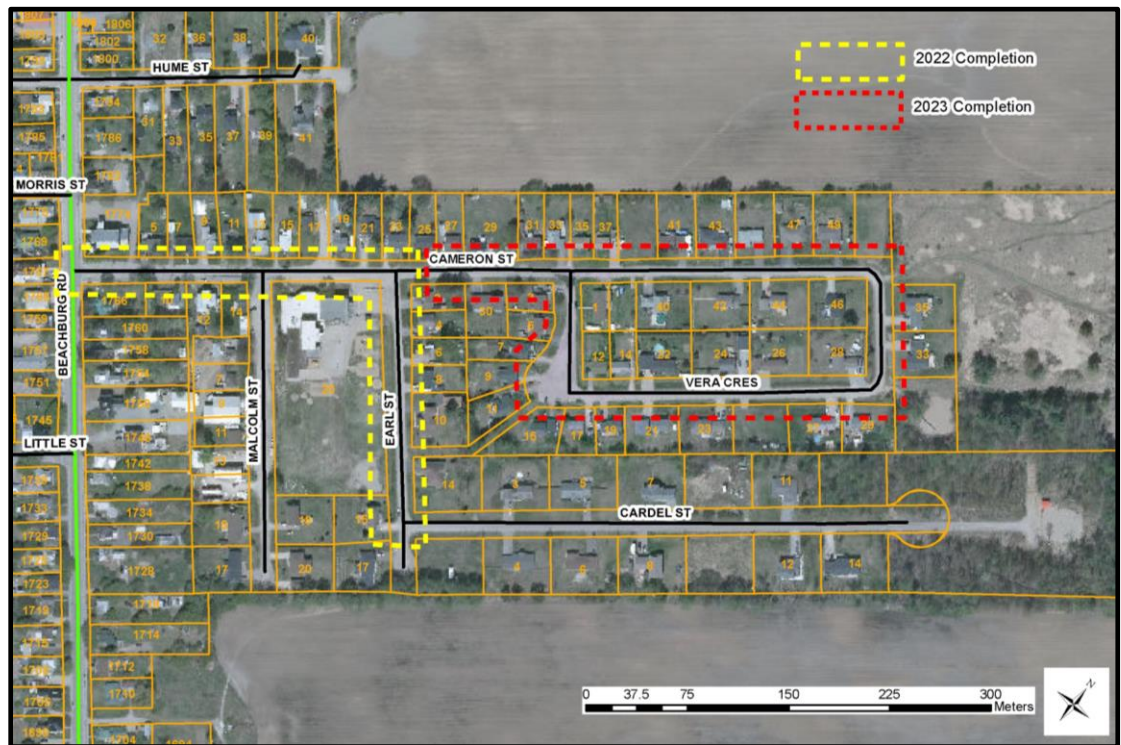

2-Week Look Ahead

- Base installation
- Curbs
- Sidewalk

Questions and Concern

H&H Construction, Council and Township staff would like to thank for your patience with the construction project. If you have any concerns related to the project, please let us know by contacting the project manager noted below.

Please encourage your neighbours to sign up for the project notices at www.whitewaterregion.ca/projects/beachburg.

Lane Cleroux
Manager of Public Works
Phone: (613) 646-2282 ext. 128
E-mail: lcleroux@whitewaterregion.ca



(613) 646-2282

P.O. Box 40
44 Main Street
Cobden, ON
K0J 1K0



www.whitewaterregion.ca

